

SafeD Translate Bot - Visual Project Timeline




Gantt Chart Representation

WEEK 1: PLANNING & ARCHITECTURE (35 hours)


[illegible]

Key Deliverable: ✓ Architecture Document, API Specs, Test Plan

WEEKS 2-4: CORE DEVELOPMENT (85 hours)


Backend Dev 1		Translation Service (15h) OCR Service (12h) File Processing (8h)
Backend Dev 2		API Development (15h) Bot Core (12h) Database & Storage (8h)
Frontend Dev		Bot Interface (10h)
QA Tester		Test Cases (5h)


Key Deliverable: ✓ Core Backend Services, API Endpoints, Bot Fea

Week 8:  6h - Documentation & Deployment

Total: 80 hours  100%


FRONTEND DEVELOPER (80 hours total)


Week 1:  10h - UI/UX Planning


Week 2:  6h - Bot Interface Design (Part 1)


Week 3:  4h - Bot Interface Design (Part 2)

Week 4: -- 0h - (Buffer/Review)

Week 5:  15h - Admin Dashboard Development


Week 6:  10h - User Interface Enhancements

Week 7:  10h - UI/UX Refinement

Week 8:  10h - Final Polish & Documentation

Total: 80 hours  100%


QA TESTER (40 hours total)


Week 1:  5h - Test Strategy Planning


Week 2:  3h - Test Case Development


Week 3:  2h - Test Environment Setup

Week 4: -- 0h - (Preparation)

Week 5:  5h - Integration Test Planning

Week 6:  6h - Testing Execution Phase 1

Week 7:  15h - Comprehensive Testing

Week 8:  4h - Final Validation & Reports

Total: 40 hours  100%

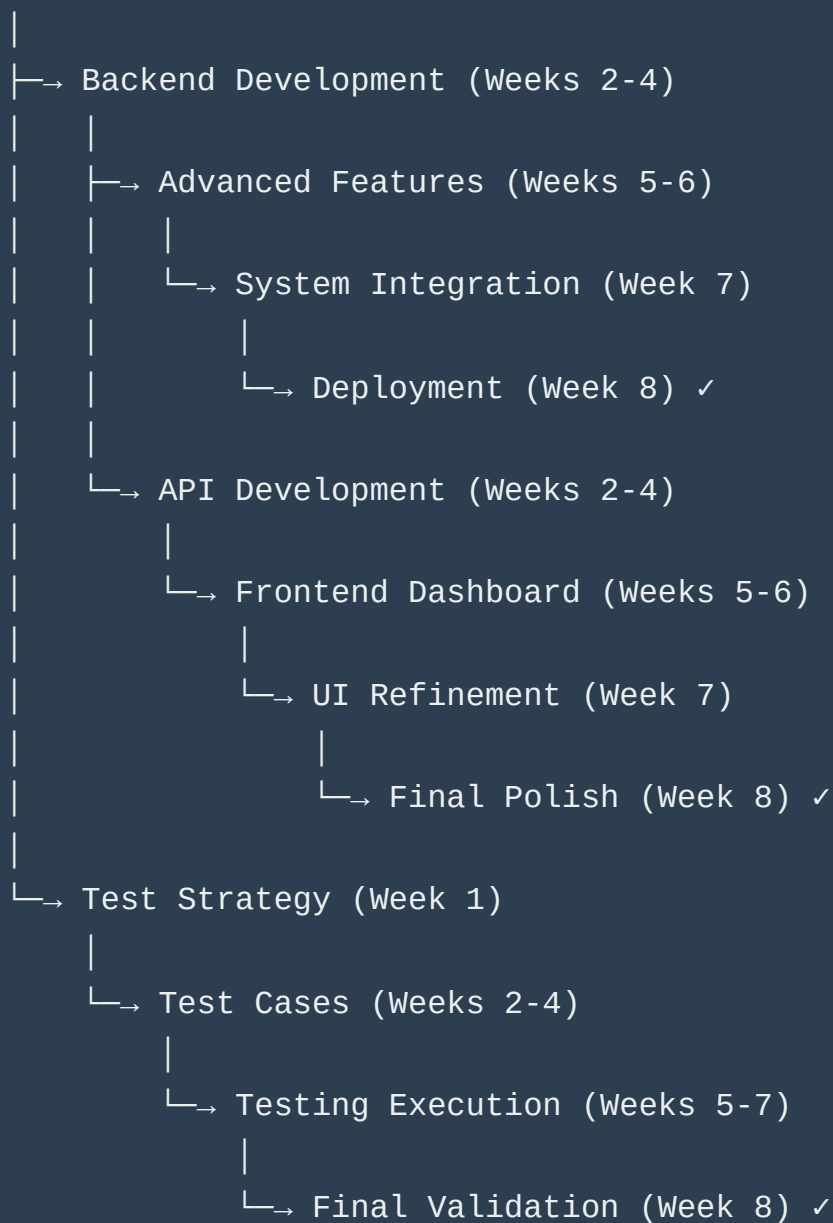
Critical Path Analysis

PROJECT CRITICAL PATH

START → Week 1 → Weeks 2-4 → Weeks 5-6 → Week 7 → Week 8 → END

Critical Dependencies:

1. Architecture Design (Week 1)

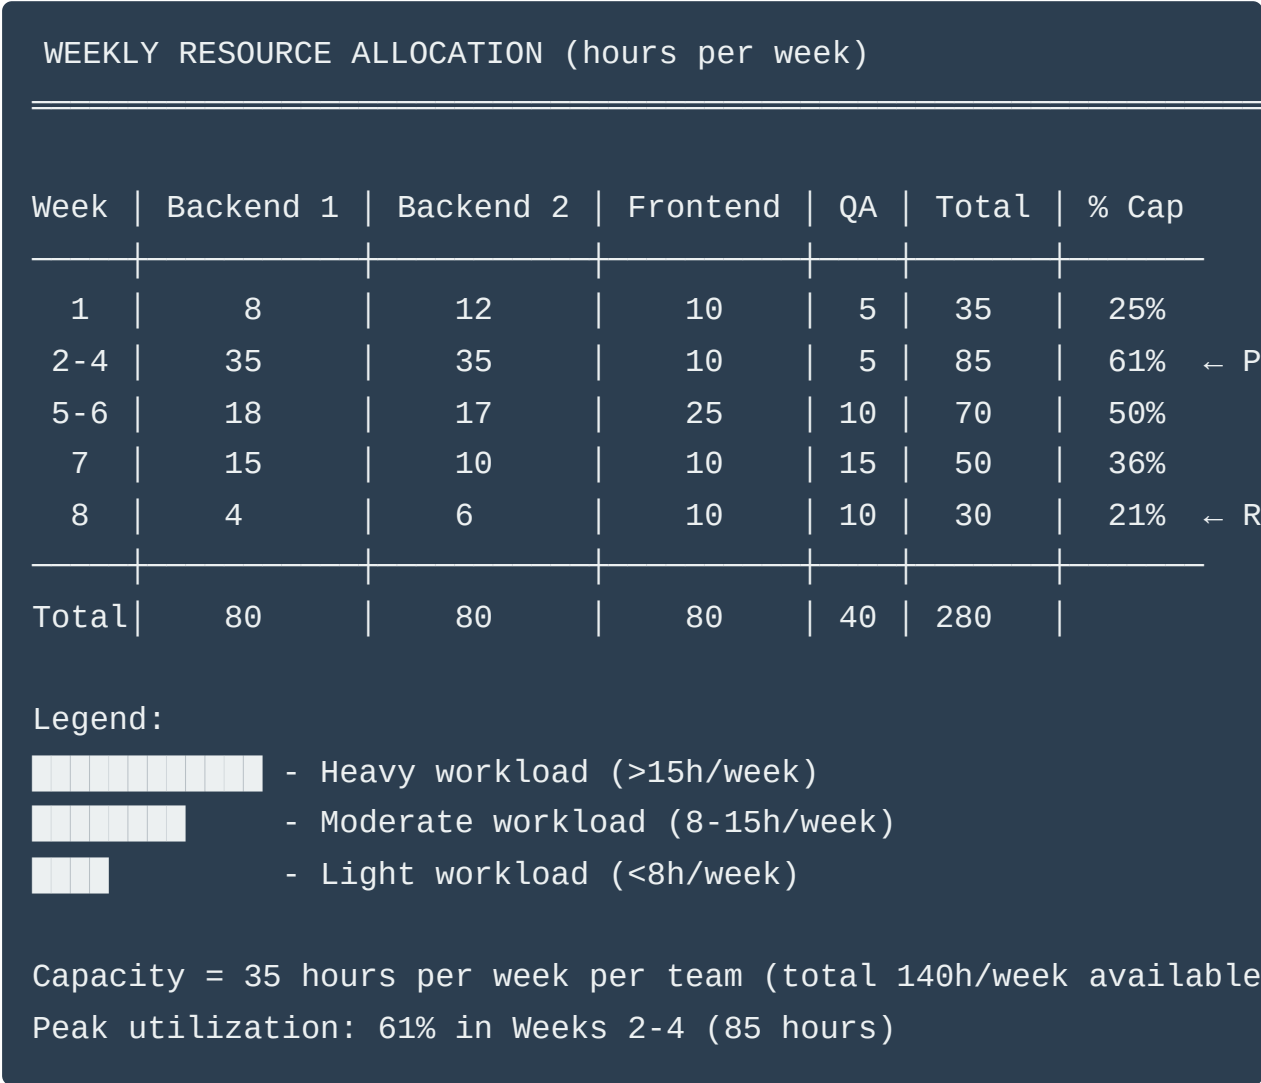


BLOCKER RISKS:


- API Development delays affect Frontend Dashboard (Week 5-6)

- Backend Integration issues delay Testing (Week 7)
- Critical bugs in Week 7 may push deployment timeline

Resource Utilization Chart



Milestone Timeline



Dependency Matrix

TASK DEPENDENCIES		
Task	Depends On	Blockers
Architecture Design	-	All
Requirements Analysis	-	Design
API Specifications	Architecture	API D
Translation Service	Architecture	Advan
OCR Service	Architecture	Docs
API Development	API Specs	Front
Bot Core	Architecture	Testi
Database Setup	Architecture	All d
Bot Interface	Bot Core	UI En
Admin Dashboard	API Dev, Backend	Testi
Analytics System	Database, API	Repor
System Integration	All Backend, Frontend	Deplo
Testing	Features complete	Deplo
Documentation	Features complete	Launc
Production Deployment	Testing, Docs	-
Critical Path: Architecture → API → Dashboard → Integration → De		

Daily Standup Template

DAILY STANDUP AGENDA (15 minutes)

Date: _____ Week: ____ Day: ____

ROUND-ROBIN UPDATES:

Backend Developer 1:

└ Yesterday: _____

└ Today: _____

└ Blockers: _____

Backend Developer 2:

└ Yesterday: _____

└ Today: _____

└ Blockers: _____

Frontend Developer:

└ Yesterday: _____

└ Today: _____

└ Blockers: _____

QA Tester:

└ Yesterday: _____

└ Today: _____

└ Blockers: _____

PARKING LOT (defer to after standup):

☐ _____

☐ _____

ACTION ITEMS:

☐ _____

☐ _____

Sprint Planning Grid

2-WEEK SPRINT STRUCTURE

Sprint 1 (Weeks 1-2): Foundation

Story Points: 35 Capacity: 70h

- Architecture & Design
- Initial API Setup
- Translation Service Foundation

Sprint 2 (Weeks 3-4): Core Features

Story Points: 40 Capacity: 50h

- Complete Translation Service
- OCR Implementation
- File Processing
- Bot Core Enhancement

Sprint 3 (Weeks 5-6): Advanced Capabilities

Story Points: 45 Capacity: 70h

- Admin Dashboard
- Analytics System
- Advanced Translation Features
- Integration Work

Sprint 4 (Week 7): Hardening

Story Points: 30 Capacity: 50h

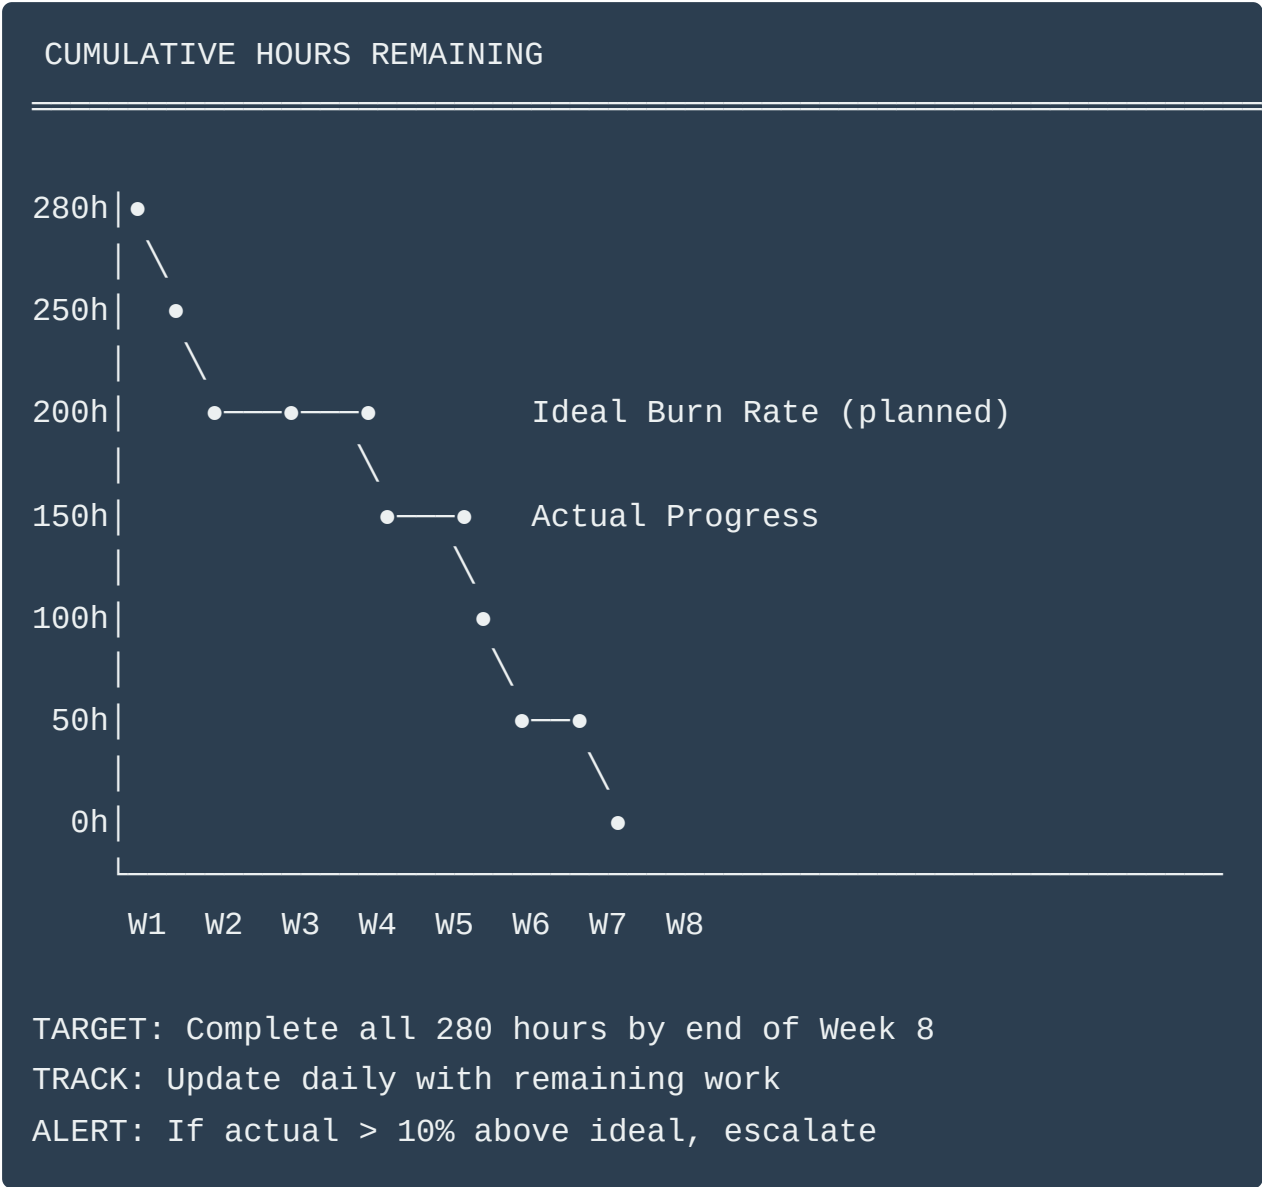
- System Integration
- Bug Fixes
- Performance Optimization
- Security Hardening

Sprint 5 (Week 8): Launch

Story Points: 25 Capacity: 40h

- Production Deployment
 - Documentation
 - Final Testing
 - Go-Live Support
-

Burn-Down Chart Template



Status Reporting Template

WEEKLY STATUS REPORT

Week: _____ | Date: _____ | Report By: _____

SUMMARY:

Overall Status: ● On Track | ● At Risk | ● Delayed

ACCOMPLISHMENTS THIS WEEK:

- ✓ _____
- ✓ _____
- ✓ _____

PLANNED FOR NEXT WEEK:

- ☐ _____
- ☐ _____
- ☐ _____

METRICS:

Hours Completed: _____ / _____ (____% of sprint)

Tasks Completed: _____ / _____

Bugs Fixed: _____

Bugs Open: _____

RISKS & ISSUES:

- CRITICAL: _____
- WARNING: _____
- INFO: _____

BLOCKERS:

- ☐ _____

HELP NEEDED:

- ☐ _____

NEXT MILESTONE: _____ (Date: _____)

This visual timeline should be used in conjunction with `PROJECT_ROADMAP.md` and `PRESENTATION.md` for complete project planning.

Last Updated: 2026-04-24
